100%

CALGARY BOARD OF EDUCATION NEW/MODERNIZED FACILITY CONSTRUCTION STATUS April 18, 2023

Building	Opening Date	Notes/Comments	
33. Northern Lights School (Coventry Hills)	Sept. 8,	Design and specifications	100%
Grades K-4 Capacity 600 students	2020	Construction Award Construction Progress Note: Project Managed by Alberta Infrastructure. School complete; warranty issue remediation underway.	100%
34. Sibylla Kiddle School (Cranston) Grades K-4 Capacity 600 students	Sept. 8, 2020	Design and specifications Construction Award Construction Progress Note: Project Managed by Alberta Infrastructure. School complete; warranty issue remediation underway.	100% 100% 100%
55. Dr. Freda Miller School Evergreen) Grades K-4 Capacity 600 students	Sept. 8, 2020	Design and specifications Construction Award Construction Progress Note: Project Managed by Alberta Infrastructure. School complete; warranty issue remediation underway.	100% 100% 100%
36. Mahogany School	Sept. 1,	Design and Specifications Construction Award	100%

36. Mahogany School Grades K-4 Capacity 600 students	_	Design and Specifications
	Sept. 1,	Construction Award
	2022	Construction Progress
		Note: Project managed by Alberta Infrastructure. School
		complete: warranty issue remediation underway

37. Prairie Sky School Grades K-9 Capacity 900 students	April 3, 2023	Design and Specifications Construction Award Construction Progress Note: Project managed by Alberta Infrastructure. Interior finishes completed, landscaping starting in Spring	100% 100% 97%
		finishes completed, landscaping starting in Spring,	

Prepared by FES Page 1 of 3

CALGARY BOARD OF EDUCATION NEW/MODERNIZED FACILITY CONSTRUCTION STATUS April 18, 2023


Building	Opening Date	Notes/Comments	
3. Lakeshore School	Oct. 11	Design and Specifications	100%
rades 5-9	2022	Construction Award	100%
Capacity 900 students		Construction Progress	100%
		Note: Project managed by Alberta Infrastructure.	10070
		Correction of deficiencies ongoing, exterior landscapes to be completed spring 2023.	
9. North Calgary HS	Aug. 31,	Design and Specifications	100%
rades 10-12	2023	Construction Award	100%
apacity 1800 students		Construction Progress	86%
		Note: Project managed by Alberta Infrastructure.	
		Building envelope nearly complete, electrical and	
		mechanical ongoing, gym floor installation started, interior masonry complete, millwork installation ongoing.	
		masonly complete, minioric installation origining.	
. Bayside School	Sept. 1	Design Build - Basis of Design/Bid package	100%
rades K-4	2022	Construction Award	100%
apacity 600 students		Design and Specifications	100%
		Construction Progress	100%
		Note: Project managed by Alberta Infrastructure. School complete; warranty issue remediation underway.	
1. Evanston School	TBD	Design Build - Basis of Design/Bid package	35%
. Evansion School			
		Construction Award	0%
ades 5-9		Design and Specifications	0%
ades 5-9			
rades 5-9 apacity 900 students		Design and Specifications	0%
rades 5-9		Design and Specifications Construction Progress Note: Project managed by Alberta Infrastructure.	0%
rades 5-9 apacity 900 students 2. Louise Dean School	Fall	Design and Specifications Construction Progress Note: Project managed by Alberta Infrastructure.	0% 0% 12%
ades 5-9 upacity 900 students 2. Louise Dean School	Fall 2024	Design and Specifications Construction Progress Note: Project managed by Alberta Infrastructure. Preliminary design underway	0%
rades 5-9 apacity 900 students 2. Louise Dean School		Design and Specifications Construction Progress Note: Project managed by Alberta Infrastructure. Preliminary design underway Design and Specifications Construction Award Construction Progress	0% 0% 12%
rades 5-9 apacity 900 students 2. Louise Dean School		Design and Specifications Construction Progress Note: Project managed by Alberta Infrastructure. Preliminary design underway Design and Specifications Construction Award Construction Progress Note: Project managed by Calgary Board of Education	0% 0% 12% 0%
rades 5-9		Design and Specifications Construction Progress Note: Project managed by Alberta Infrastructure. Preliminary design underway Design and Specifications Construction Award Construction Progress	0% 0% 12% 0%
rades 5-9 apacity 900 students 2. Louise Dean School		Design and Specifications Construction Progress Note: Project managed by Alberta Infrastructure. Preliminary design underway Design and Specifications Construction Award Construction Progress Note: Project managed by Calgary Board of Education	0% 0% 12% 0%

Prepared by FES Page 2 of 3

CALGARY BOARD OF EDUCATION NEW/MODERNIZED FACILITY CONSTRUCTION STATUS April 18, 2023

Building	Opening Date	Notes/Comments
44. Annie Gale School Grades 6-9 Modernization	TBD	Note: Planning approved on March 1, 2023 Awaiting for further details from AB Ed and AB Infra.
45. Cornerstone High School TBD	TBD	Note: Planning approved on March 1, 2023 Awaiting for further details from AB Ed and AB Infra.
46. A.E. Cross School Grades 7-9 Modernization	TBD	Note: Pre- Planning approved on March 1, 2023 Awaiting for further details from AB Ed and AB Infra.
47. Sir John A. MacDonald School Grades 6-9 Modernization	TBD	Note: Pre- Planning approved on March 1, 2023 Awaiting for further details from AB Ed and AB Infra.
48. Saddle Ridge Middle School TBD	TBD	Note: Pre- Planning approved on March 1, 2023 Awaiting for further details from AB Ed and AB Infra.

Prepared by FES Page 3 of 3

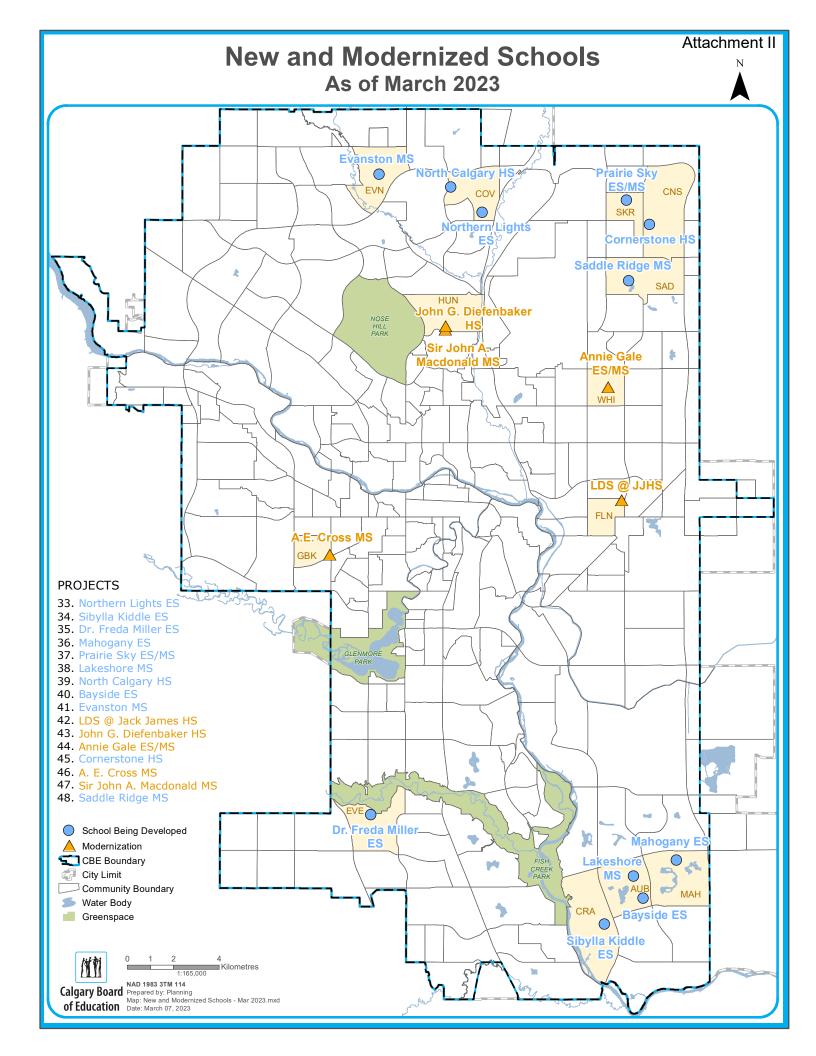

North Calgary High School



West Elevation – Library & entrance



North-West Elevation (classroom wing)



Solar panels - south roof



2nd Floor hallway - classroom wing



Gathering Space – 2nd floor balcony



Computer Lab

Prairie Sky School



Main Entrance - North elevation



Foods Lab




Classroom – Middle school (typical)



Wet Lab – Elementary (typical)



Gathering Area



Main Gym
